

Missoula Mercantile Project


Weekly Report-2-27-17

Destruction Phase

On-Site Activity:

Monday: 2-27-17

1. The crew working on clean-up second floor area with all the ceiling joists removed and lath and plaster drop down onto the floor this must be cleaned up so work can begin on removing the second floor.
2. Light snow been pushed off the roof area the sheeting here will be removed.
3. Area worked on last week the ceiling joists will be removed today.
4. Picture indicates that the crew has removed all of the ceiling joists in this area. Note that at-this-time in the afternoon light snow was falling.
5. The section that the snow has been pushed out of the way the roof sheeting was taken up.
6. Timber in the staging area shows a lot of square nails have been used in all sections of construction of this building.
7. Staging area in the parking lot, this material has been banded, it is in the process of being loaded and removed from the site today. Note this time in the afternoon the sun is out and the snow stopped and a lot of it has melted away.
8. A load of material removed from the site today.

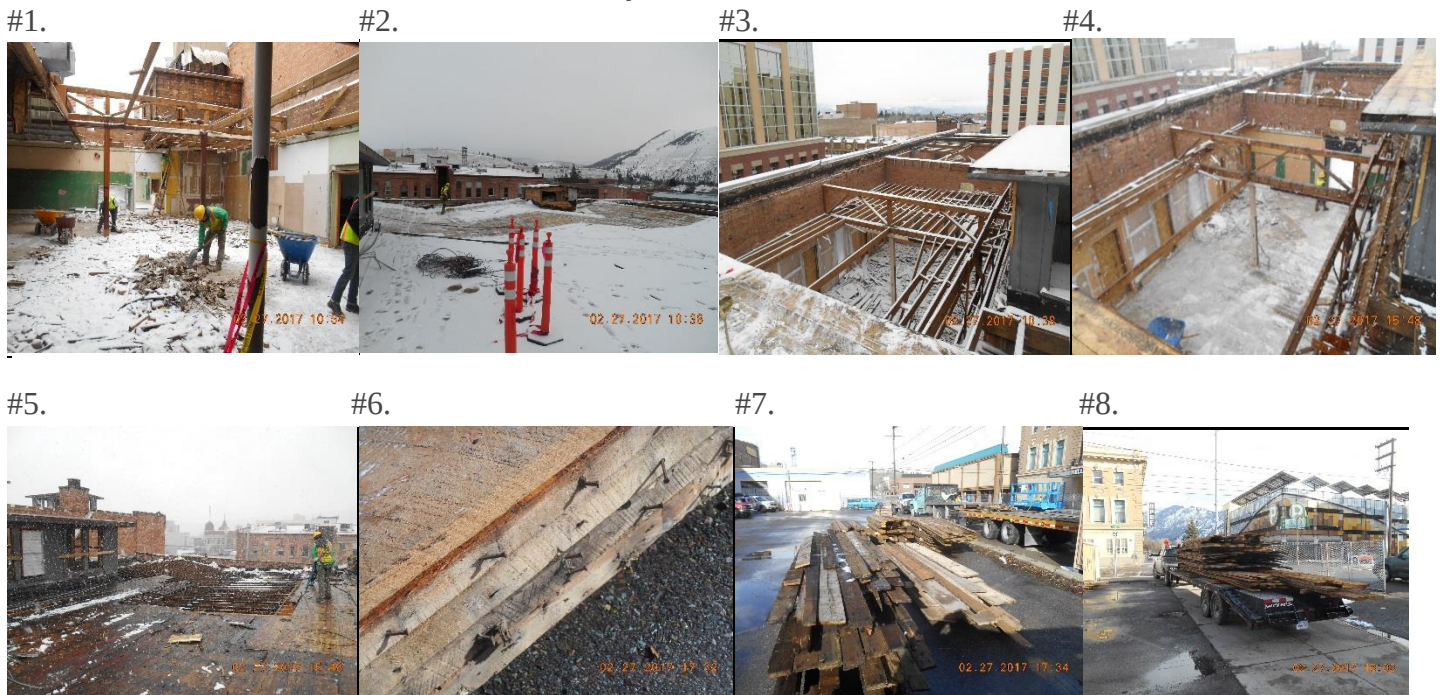

Missoula Mercantile Project


Weekly Report-2-27-17

Destruction Phase

On-Site Activity:

TUESDAY: 2-28-17

1. This is the upper section of roof the larger section, just about half, the crew will have all of this sheeting removed by the end of the day.
2. This picture shows that a lot of the roof joists have been removed, exposing the ceiling joists below, note: the structure of the valley and peaks are used to move the water to the roof scupper.
3. This section has most of the roof sheeting removed. The crew will start removing the roof joists, note: the valley configuration in this location.
4. This is about half of the roof section. The larger section the goal is to completely finish this large section of roof by the end of the week.. The sheeting will be removed, off all of the roof joists to be removed down to the ceiling joist below.
5. Second-floor post and beam configuration, background shows that most of the ceiling has been removed. This will make an easy chore for the crew to remove these ceiling joists.
6. With the sheeting removed, part of the roof joists also have been removed, this is the area that they started on this morning at 8 o'clock.
7. This half of the upper roof has been nearly cleared of all of the roof joists exposed. Note: the ceiling joists some of these or about 30 feet long.
8. Load of material ready to leave the site. This is occurring daily.

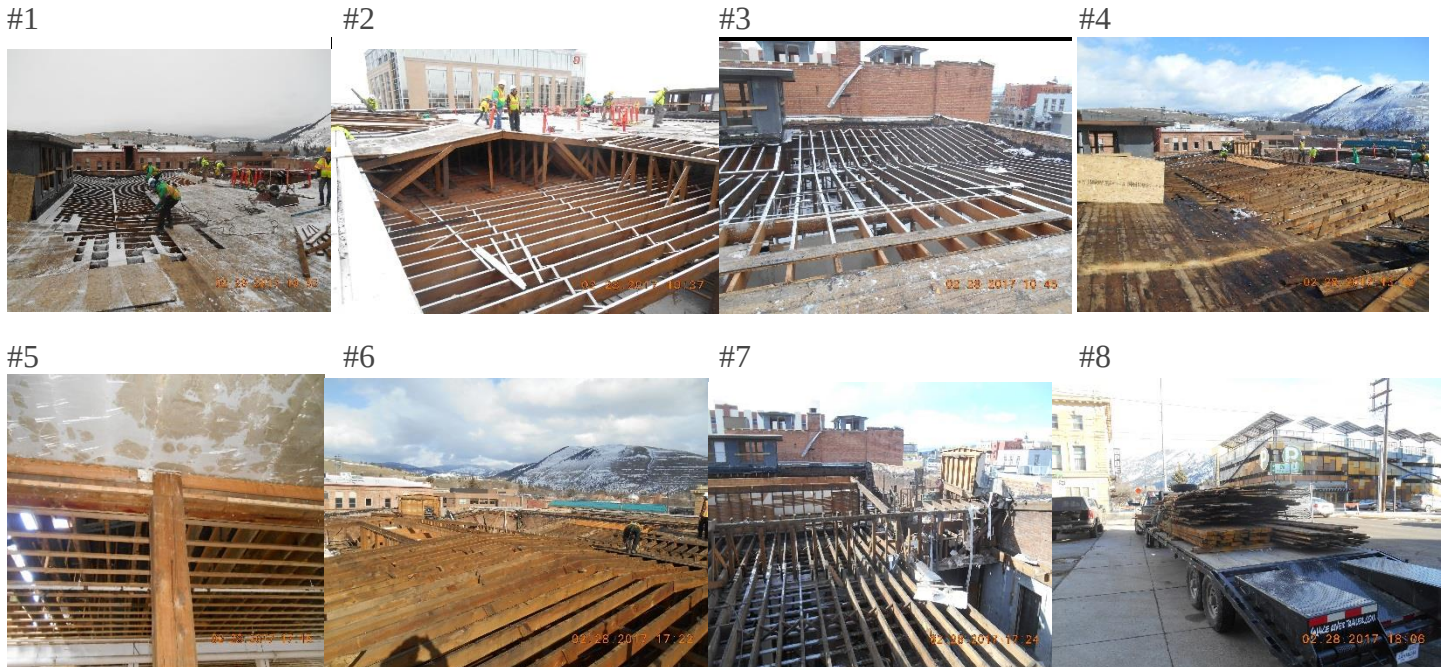

Missoula Mercantile Project

Weekly Report-2-27-17

Destruction Phase

On-Site Activity:

Wednesday: 3-01-17

1. Staging area pretty depleted right at-this-time. More material will be coming down from the roof area today.
2. Second floor area with a lot of the other loose debris has been drop down. This floor will be cleaned up then the ceiling joists will be lowered down and removed to the staging area.
3. This is the second half of the upper roof section which will be worked on today. The goal is to completely finish this large area down to the ceiling joists by Friday.
4. Upper section of roof will be worked on today. Most of the sheeting will be removed by the end of the day..
5. Crew is working on getting ready to remove these ceiling joists down to the second floor.
6. Material coming down from the roof and being loaded onto a truck and trailer.
7. Post and beam connection, note: That these beams are just sitting on the post, toe-nailed in place.
8. Load of material going out today.

#1.



#2.



#3.



#4.



#5..



#6.



#7.



#8.



Missoula Mercantile Project

Weekly Report-2-27-17

Destruction Phase

On-Site Activity:

Thursday: 3-02-17

1. Roof area and staging area shrinking daily. Crew working on removing last of the roof sheeting in this area.
2. Progress of the deconstruction from the west to east across the roof. This has been done with efficiency and a high regard for safety.
3. Material coming down off the roof staging area by use of the sky track.. Note: that we removed two of the windows in order to move material from the second floor staging area also by means of the sky track.
4. Material being removed from the second floor staging area with the boom attached to the sky track material is banded and moved from this area to the ground staging area.
5. Second floor area cleaned up. The crew will start dropping the ceiling joists down to the second floor area.
6. Material been sorted and stacked at the second floor staging area.
7. A lot of material has come down today from both the roof and second floor staging areas. All of this material will be removed from site today.
8. Second trailer load of material removed from the site.

#1



#2.



#3.



#4.



#5.



#6.



#7.



#8.



Missoula Mercantile Project

Weekly Report-2-27-17

Destruction Phase

On-Site Activity:

Friday 3-03-17

1. Material being moved from the second floor staging area.
2. Crew removing last of the roof sheeting in the largest section of roof area.
3. Crew preparing to drop all of these floor joists down to the second floor.
4. Staging area quite a lot of lumber being stacked here today.
5. With joists cut at one end and lowered by rope to the floor below, this action causes the joists to come loose at the beam support.
6. More than half of these ceiling joists have been removed from this area, staged on the second floor and then moved down below to the parking lot to be loaded out.
7. Note: the crew cleans up the area behind themselves as they proceed through each phase.
8. This picture shows the framework that has been installed below one of the old skylights the original frame with the small decorative spindles. We believe that this square lattice work held the greenish tinted glass with wire, we have retrieved some of that glass also.
9. And this is what you see looking from the second floor up, blue sky.
10. Large load of recovered material been removed from the site this afternoon.

#1.



#2.



#3.



#4.



#5.



#6.



#7



#8





Missoula Mercantile Project

Weekly Report-2-27-17

Destruction Phase

On-Site Activity:

Friday 3-03-17

#9.

#10.



-

-

